



Bannock Utility Coordinating Council
3636 Jason Avenue | Pocatello, ID 83204
Phone (208) 681-9228

Merril Quayle, President
JJ Murphy, Vice President
Bridger Morrison, Secretary/Treasurer

Bannock Utility Coordinating Council

Meeting Minutes
August 14, 2019
10:00 a.m.

City Hall – Paradise Conference
Room

Bannock Utility Coordinating Council Meeting Minutes

August 14, 2019 10:00 a.m.

City Hall – Paradise Conference Room

1. Welcome/Attendees Sign-In

- Meeting was called to order by Merrill Quayle, Bannock UCC President, at 10:00 a.m.
- Attendees: **See Attachment A**
- Excused: Clair Stucki (Idaho Power), Derek Covington (Trufiber), Robbie Austin (Mickelsen Construction)

2. Approval of Minutes from the July 10th meeting

Council was asked to approve the minutes from the July 10th meeting as written. Motion to approve made by Melodie Halstead and seconded by Kim Hunter.

3. September 11th Meeting Time Discussion

Merril will be out of town the week of our regularly scheduled meeting. A vote was taken to cancel the September meeting. Motion to approve made by JJ Murphy and seconded by Melodie Halstead.

4. Financial Report

As of the end of June, the BUCC account has a balance of \$1,393.07.

5. Items from Idaho UCC

- The IUCC Fall meeting will be held on September 12 – 13 in Boise at the Intermountain Gas Conference Center. The meetings are usually Thursday afternoon and Friday morning. If you are going to attend just one day, Thursday afternoon is recommended.
- Bob Chandler is the IUCC website person, he can be reached at bobchandlercda@gmail.com

6. Dig Line Information and News

- Ticket Data – **See Attachment B**
- July has been another extremely busy month for the excavating community across the state of Idaho. Compared to July 2018, Digline has processed over 19% more locate requests in our service area. Overall, year-to-date, there has been an 11% increase in locate requests compared to 2018.

7. Damage Prevention Board News

- The Division of Building Safety recently began a marketing campaign with the Safe Excavator Initiative, featuring Mike Rowe from Dirty Jobs. This campaign will run until at least Oct. 19th. This message is being shown on TV around the state along with various radio stations. The web site for the Safe Excavator Initiative is: www.safeexcavator.com/idaho if you want to take a look. It is still a work in

progress however there are a couple of videos with Mike Rowe so you can see what the DP Board is putting out there for education.

- Link to the meeting dates and agendas
<https://dbs.idaho.gov/boards/dpboard/dpmeetings.html>
- Jerry Peterson is no longer with the Damage Prevention Board. They will notify us when his replacement is announced.

8. Open Discussion on Projects Within the Area of Influence

Cable One (Kim Hunter):

- Fiber in the Fairway/Gate City Elementary area
- Fiber where Green Tea used to be/new FBI building

ITD (Melodie Halstead):

- Project Report – **See Attachment C.** New projects have been added. Please make sure to take a look at the design section of the project report.

Marathon Pipeline (Frank Delos Reyes):

- Previously Andeavor, now Marathon Pipeline (MPLX)
- Boring of Chevron pipeline

Williams (Cody Cordell):

- Cody and another rep will be coming to our meetings now that Guy is retired. See the sign-in sheet for contact information.
- No projects to report at this time.

Bannock County (Caryn Havlovick & Brett Grayson):

- Westfield Estates Division 1 off of Chubbuck Road is under construction

Idaho Power (Ethan Morgan):

- Ethan is based out of Boise and will be alternating visiting various UCC in Southern Idaho. He is responsible for taxpayer funded projects. See the sign-in sheet for his contact information.

City of Chubbuck (Bridger Morrison):

- Two more phases of Brookstone Subdivision are in review

Idaho Gas Co. (JJ Murphy):

- Cowboy Trailer Court – finishing in another week or two
- Joint Trench
- Projects in Blackfoot

Utility Vac-N-Fill (Kirsten Bringhurst):

- Still working in Wyoming – hydrants through campgrounds at Grand Teton

JUB Engineers (Andrea Sheppard):

- Hawthorne/Quinn Intersection
- City Council approved the Pocatello HS updates so that will be moving forward

Syringa Networks (Frank Warr):

- Center Street/18th Way – bore on 17th/18th is all that left
- Maple Street/Gary

City of Pocatello (Merril Quayle):

- Subdivisions in Review/City Council:
 - Mather
 - New Bounds
 - Armstrong Legacy Division 2
 - Crestview Cove
- Waiting Construction:
 - Riverside Green Townhouse 4th Addition (Preliminary)
 - Juniper Reserve Division 3 & 4 (Preliminary)
 - Northgate District Division 1
- Subdivisions under Construction
 - The Crossings Division 2
 - Stratten Estates Division 1
 - Breezy Pointe Division 3 & 4
- Reported working on the following projects:
 - Benton Street Bridge continuing construction through 2019
 - Hawthorne and Quinn - working on right-of-way acquisition and starting to coordinate utility relocation.
 - Centennial Park and River Vision continuing.
- Street Department
 - Pavement Rehabilitation under way, see prior schedule.
 - Pavement marking and cross walks.
- Water Department
 - 2019 & 2020 projects map – **See Attachment D**
- WPC
 - Fairground Sanitary Sewer Extension Project started this week.
- Other
 - Pre-construction on utility projects
 - Call for inspections
 - Patching 72 hours

9. Any other items from the council

N/A

10. Review of any action items

N/A

11. Next meeting

Scheduled for Wednesday, October 9th at 10:00 a.m.

12. Adjourn

Meeting adjourned by Merrill Quayle at 10:36 a.m.

APPROVED BY:

MERRIL QUAYLE, PRESIDENT

ATTEST:

BRIDGER MORRISON, SECRETARY/TREASURER

PREPARED BY: Brenda Andrews

ATTACHMENT

A

ATTACHMENT B



Total Ticket Summary - Inbound

Month	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019
Jan	2,726	2,858	2,806	2,568	3,944	4,078	4,400	2,864	5,782	7,651
Feb	3,119	2,922	3,650	3,660	4,203	5,908	6,225	5,546	6,813	5,565
Mar	5,959	4,925	5,171	6,390	7,775	9,477	9,929	10,926	10,246	12,035
Apr	7,752	6,925	7,538	9,072	10,123	10,822	11,643	11,719	14,030	16,229
May	7,322	8,027	8,759	9,650	10,145	9,891	11,791	13,726	15,147	15,838
June	7,445	7,948	7,822	8,322	9,896	10,839	11,894	13,057	13,585	14,410
July	6,946	6,574	7,079	8,393	9,264	10,076	10,201	11,520	12,839	15,322
Aug	6,475	7,013	7,555	8,328	8,318	9,516	11,965	12,589	13,565	
Sept	6,638	6,529	7,125	7,770	8,453	9,884	11,270	10,434	11,711	
Oct	5,684	6,151	7,634	7,705	8,155	8,780	9,888	11,363	13,309	
Nov	4,135	4,371	5,012	5,030	5,062	6,055	8,069	8,314	9,486	
Dec	2,617	2,956	3,150	3,064	4,408	4,245	3,749	5,192	5,582	
Yearly Totals	66,818	67,199	73,301	79,952	89,746	99,571	111,024	117,250	132,095	87,050

ATTACHMENT C

IDAHO TRANSPORTATION DEPARTMENT
DISTRICT FIVE MONTHLY PROJECT REPORT- JULY 2019

CONSTRUCTION

Project Name: Bear River Bridge
Key: 13559 **Route:** SH-36 **Mile Post:** 130.91 **Eng A**
Counties: Franklin **BID:** \$3,403,618.17
Contractor: DL Beck, Inc.
Project: Bridge Replacement
Status: With the construction completed, the contractor finalizing the removal of the piers found in the river from the original bridge.
The district is currently going through the project for closeout.

Project Name: McCammon IC #47 to Inkom IC #56
Key: 19580 **Route:** I-15 **Mile Post:** 46.67-56.4 **Eng A**
Counties: Bannock **BID:** \$ 8,906,918.84
Contractor: JB Parsons, Inc.
Project: Pavement rehabilitation mill and inlay
Status: Project is completed and traffic is back to normal 2 lane traffic in each direction.
Last coat of paint and delineators are all that is left to complete.

Project Name: US-89, 12th St. Opass to JCT US-30, Montpelier
Key: 20155 **Route:** US-89 **Mile Post:** 25.294 – 25.984 **Eng A**
Counties: Bear Lake **BID:** \$1,656,596.00
Contractor: Staker & Parson Comp dba Jack B. Parson
Project: Mill & Inlay with striping changing from a 2 lane each direction to a 1 lane each direction with a 2-way turn lane with parallel parking on each side. This project includes new sidewalk down US-30 (4th Street) from South of Garfield Street to Boise St.
Status: Project is complete except for applying a seal coat. The contractor plans to apply the seal coat in August.

Project Name: Shelley NCL to York Road
Key: 09225 **Route:** US-91 **Mile Post:** 118.7 – 122.9 **Eng B**
Counties: Bingham/Bonneville **BID:** \$1,799,499.70
Contractor: Knife River Corporation – Northwest
Project: R/W Acquisition, widening
Status: Canal bridge is complete. R/W is still in the process of being purchased and utilities are being designed and moved. Next project Key 19376 will start in Oct 2020 to expand to 5 lanes.

Project Name: FY18 D5 Bridge Repair
Key: 18828 **Route:** I-15 **Mile Post:** Various **Eng B**
Counties: Various **BID:** \$2,081,804.70

Contractor: Cannon Builders, Inc.
Project: Bridge Preservation on five separate bridges: Jensen Road I-15 MP 44.08; N McCammon IC I-15 MP 47.16; Portneuf River I-15 MP 55.61; Robin Road I-15 MP 45.82; and Virginia IC I-15MP 42.41.
Status: Construction underway. Anticipated to be completed July 2019.

Project Name: Tincup Cr. Br,
Key: 18853
Routes: SH-34
Counties: Caribou
Mile Post: 108.8
BID: \$1,922,506.80
Eng B
Contractor: Cannon Builders
Project: Bridge Replacement
Status: Project underway Time Suspended until Summer 2019 to finish the sealcoat operation.

Project Name: Tincup Creek Bridge
Key: 19579
Routes: SH-34
Counties: Caribou
Mile Post: 106.4
BID: \$3,665,504.45
Eng B
Contractor: Cannon Builders
Project: Bridge Replacement
Status: companion to 18853.

Project Name: SH-38, Malad, 50 South St
Key: 19970
Routes: SH-38
Counties: Oneida
Mile Post: 0.000 – 0.689
BID: \$1,302,798.00
Eng B
Contractor: Staker & Parson Companies dba Idaho Materials and Construction
Project: Pavement Rehabilitation
Status: A was held April 10th. Work on ADA Ramps and sidewalk is ongoing. Paving was completed in June. A change order is in the works to modify the Southbound off-ramp in Malad. This project is anticipated to be completed by the end of September 2019.

Project Name: I-15, Wye to Fort Hall Bndry
Key: 20064
Routes: I-15
Counties: Bannock
Mile Post: 72-76
BID: \$6,884,000.00
Eng B
Contractor: Western Construction Inc.
Project: CRABS
Status: Project has begun and is anticipated to be completed by the end of July 2019.

Project Name: Rose IC
Key: 14002
Route: I-15
Counties: Bingham
Mile Post: 97.681
BID: \$10,843,118.88
Eng C
Contractor: Cannon Builders, Inc.
Project: Bridge Replacement
Status: Riverside Canal construction complete. 1st phase girders to be set early June.

Project Name: Lateral A Canal,

Key: 18891 **Route:** SH-39 **Mile Post:** 41.45 **Eng C**
Counties: Bingham **BID:** \$620,988
Contractor: Knife River Corporation – Northwest
Project: Bridge Replacement
Status: Construction wrapping up.

Project Name: **Portneuf River Br,**
Key: 19019 **Route:** US-30 **Mile Post:** 365.174 **Eng C**
Counties: Bannock **BID:** \$3,325,502.19
Contractor: **DL Beck, Inc.**
Project: Culvert Replacement
Status: Concrete Liner complete in center pipe. Tunnel lining work in the main culvert underway. Tentatively scheduled for completion in July.

Project Name: **FY19 Franklin County Pavement Preservation**
Key: 19085 **Route:** **Mile Post:** **Eng C**
Counties: Franklin **BID:** \$3,665,504.45
Contractor: **Staker & Parson Comp dba Jack B. Parson**
Project: **Pavement Preservation**
Status: Sealcoats complete. Awaiting contractor repairs to minor areas of damage.

Project Name: **Georgetown Summit to Nounan Road**
Key: 19382 **Routes:** US 30 **Mile Post:** 419.124 - 424.582 **Eng C**
Counties: Bear Lake **BID:** \$7,389,542.00
Project: Reconstruction
Status: Construction is under way and going according to schedule. This project is anticipated to be complete first of October.

Project Name: **Bannock Co Line to Lund**
Key: 19926 **Route:** US-30 **Mile Post:** 371.5 to 376 **Eng C**
Counties: Bannock, Caribou **BID:** \$2,384,311.08
Contractor: **Kilgore Companies LLC DBA Legrand Johnson Construction Co.**
Project: Pavement rehabilitation mill and inlay, Drainage Repair
Status: Project complete. Seal coat warranty repairs to be made in conjunction with 19324.

Project Name: **Aberdeen Canal,**
Key: 18959 **Route:** US-26 **Mile Post:** 301.41 **Eng C**
Counties: Bingham **BID:** \$1,842,621.28
Contractor: Cannon Builders, Inc.
Project: Bridge Replacement
Status: Awarded to Cannon Builders. Will be constructed starting in the fall of 2019.

Project Name: **Sheeptrail to Hoff Rd**
Key: 19992 **Route:** US-39 **Mile Post:** Various **Eng C**
Counties: Bingham **BID:** \$1,998,711.78
Contractor: Staker Parson.
Project: Pavement Rehabilitation
Status: Will be constructed starting in June of 2019.

Project Name: **FY19 South Bannock County Pavement Preservation**

Key: 19324 **Route:** **Mile Post:** **Varies** **Eng C**
Counties: **Bannock** **BID:** \$4,768,536.72
Contractor: Kloepfer, Inc.
Project: **Pavement Preservation**
Status: Kloepfer, Inc was the lowest bidder. Will begin summer 2019.

Project Name: **I-86, Raft River to Rockland IC# 36**
Key: 19824 **Route:** **I-86** **Mile Post:** **Eng C**
Counties: Power **BID:** \$2,478,840.30
Contractor: **Cannon Builders**
Project: Preserve Concrete from MP 14.808 to 35.94.
Status: On shelf and scheduled for construction in 2020.

Project Name: **Northgate IC, Chubbuck**
Key: 20314 **Routes:** I-15 **Mile Post:** 73.5 **Materials/Traffic**
Counties: Bannock **BID:** \$13,132,785.04
Contractor: **Cannon Builders**
Project: New Interchange
Status: Work began November 5th, 2018. The Contractor has completed the Center Pier. East side and west side are now at subgrade elevation. Storm sewer and electrical conduit are going in as well. Subbase and base will be brought in starting the week of August 29th. Girders are scheduled for August 6, 7, and 8.

Project Name: **I-15, Virginia IC to Arimo SCL**
Key: 19839 **Routes:** I-15 **Mile Post:** 35.6-40.8 **Eng B**
Counties: Bannock **BID:** \$7,701,028.00
Contractor: **STAKER & PARSON COMPANIES**
Project: CRABS
Status: Project anticipated to begin Summer 2019 and be completed by the fall of 2019.

DESIGN

FY 2019

Project Name: **FY20 North Bannock County Pavement Preservation**
Key: 19867 **Route:** **Mile Post:** **Eng C**
Counties: **Bannock**
Project: Pavement Preservation
Status: On shelf. Some revisions upcoming prior to July 1st based on coordination with local stakeholders.

FY 2020

Project Name: **Bench Canal Br**
Key: 19924 **Route:** SH-34 **Mile Post:** 43.325 **Eng B**
Counties: Caribou
Project: This project will replace the Bench Canal Bridge at milepost 43.324 on SH-34.
Status: The project is PS&E ready and awaiting award

Project Name: Caribou County Line to Georgetown Summit
Key: 20051 **Route:** US-30 **Mile Post:** 415.665 – 419.124 **Eng C**
Counties: Bear Lake
Project: Pavement Preservation
Status: On Shelf.

FY 2021

Project Name: INT of I-86B and Pocatello Ave
Key: 19605 **Route:** I-86B **Mile Post:** 4.08 **Eng A**
Counties: Power
Project: This project will create a roundabout at the intersection of I-86B and Pocatello Avenue in American Falls.
Status: A series of four public open houses were held in 2017 and 2018 to solicit public input and a roundabout alternative was selected on the basis of their input. Detailed design and right of way plan preparation is underway. Design is approximately 70 percent complete. A final open house will be held August 1, 2019. Right of way will be purchased in FY 2020 and construction is scheduled for 2022.

Project Name: I-15, Arimo Road IC #40
Key: 19849 **Route:** I-15 **Mile Post:** 40.425-40.426 **Eng A**
Counties: Bannock
(#40) Bridge on I-15 in Bannock County.
Status: This is being designed by D5 and HQ Bridge sections. Bridge is currently finalizing the sub-structure design while D5 has completed the roadway design and has begun creating the plan sheets. Anticipated to be PS&E ready by Feb 2020. This is a FY2022 as it was moved back to facilitate a different project that needed to be moved forward.

Project Name: FY21b D5 Bridge Repair
Key: 19730 **Route:** I-15 **Mile Post:** Various **Eng B**
Counties: Bannock and Oneida
Project: Bridge preservation project on 11 structures: Woodruff IC (MP 2.54), Samaria Road (MP 6.1), Two Mile Road (MP 11.35), Colton Lane Road IC (MP 21.51), Bissell Lane Road (MP 23.03), Summit Road (MP 24.42), Marsh Valley Road (MP 26.77), Woodland Road (MP 29.43), Marsh Creek (MP 3018), Downey IC (MP 30.87), and Bowman Road (MP 34.01).
Status: PS&E was submitted July 18, 2019.

Project Name: US-91, Shelley NCL to York Rd, Phase 2
Key: 19376 **Route:** US-91 **Mile Post:** 118.7 – 122.9 **Eng B**
Counties: Bingham and Bonneville
Project: Widening
Status: Kickoff Meeting was held September 19, 2018. Work on design is beginning. Anticipated to be PS&E ready by September 2019.

Project Name: I-15, Inkom South IC to Portneuf IC
Key: 20229 **Route:** I-15 **Mile Post:** 56.4 – 62.5 **Eng B**

Counties: Bannock
Project: This project will be a mill and inlay. It will improve pavement conditions on I-15 between mileposts 56.4 and 62.5 by performing an asphalt replacement. This will address the aging pavement, thereby creating a stable and smooth driving surface.
Status: This project has been delayed until 2025

Project Name: **Tincup Cr. Br MP 106.818**
Key: 20457 **Route:** SH-34 **Mile Post:** 106.818 **Eng B**
Counties: Caribou

Project: This project intends to replace the structurally deficient Tin Cup bridge on SH-34 in Caribou County.

Status: Project to be PS&E by September 30, 2019 and be on the shelf ready for advertisement.

Project Name: **E Alameda Rd and Yellowstone Ave.**
Key: 19053 **Route:** US-91 **Mile Post:** 77.89 **Eng C**
Counties: Bannock

Project: **Turn Bay and signal addition**

Status: Design completed and turned in April 30, 2018. **Project moved to FY21 as part of KN 21827.**

Project Name: **Cedar to Flandro, Pocatello**
Key: 21827 **Route:** I-15B, US-91 **Mile Post:** Various **Eng C**
Counties: Bannock

Project: Pavement Rehabilitation

Status: Preliminary Design.

Project Name: **FY 21 Power County Pavement Preservation**
Key: 19603 **Route:** **Mile Post:** **Eng C**
Counties: Power

Project: Pavement Preservation.

Status: In design development phase. PS&E scheduled for late June of 2019.

Project Name: **FY 21 D5 Bridge Repair**
Key: 20142 **Route:** I-15 **Mile Post:** Various **Eng C**
Counties: Bingham, Bannock

Project: Bridge maintenance

Status: Preliminary bridge plans developed, roadway plans in development. PS&E scheduled for late May of 2019.

FY 2022

Project Name: **UPRR Inkom OPass**
Key: 20186 **Route:** I-15 **Mile Post:** 55.913-55.914 **Eng A**
Counties: Bannock

Project: This project intends to replace the UPRR Inkom Overpass Bridge in Bannock County on Interstate 15.

Status: This is being designed by HDR. HDR has completed the situation and layout of the super-structure. Borings are being completed for the sub-structure design and phase reports currently. This is large structure as it takes I15 over the I15B Loop and

several UPRR main line tracks. Preliminary design review is scheduled for fall of 2019. Anticipated to be PS&E ready by July 2020. This is a FY2023.

Project Name: I-15, Fort Hall IC #80
Key: 20083 **Route:** I-15 **Mile Post:** 79.821-80.123 **Eng A**
Counties: Bannock
Project: This project includes bridge replacements for I-15 Exit #80 (milepoint 79.9) Overhead Bridge including new ramps, Town Lateral Canal Bridge under I-15 (milepoint 80.14), and Ross Fork Creek Bridges under the Exit #80 ramps and I-15 (milepoint 79.8) It will also include redesigning the roads that are directly adjacent to the bridges to fit the new geometric design of the ramps and bridges as necessary.
Status: This is being designed by D5 and HQ Bridge sections. Bridge is currently finalizing the sub-structure design while D5 has completed the roadway design and has begun creating the plan sheets. Anticipated to be PS&E ready by Oct 2020. This is a FY2022.

Project Name: Thomas to Collins Siding Rd
Key: 20424 **Route:** SH-39 **Mile Post:** 51.451 - 52.698 **Eng A**
Counties: Bingham
Project: This project will involve the addition of a two way left turn lane, with a possible roundabout at the intersection of SH-39 and Collins Siding Road.
Status: Waiting for Blackfoot Funding in order to scope change. TBD

Project Name: SH-39, Sterling N Rd to RR XING
Key: 20455 **Route:** SH-39 **Mile Post:** 30.0 – 35.5 **Eng B**
Counties: Bingham
Project: Rehab
Status: Charter and project schedule are being developed. Kickoff Meeting was held on March 28th. Anticipated to be PS&E ready by Oct. 2020.

Project Name: I-86/I-15 System IC
Key: 20589 **Route:** I-86/I-15 **Mile Post:** **Eng B & C**
Counties: Bannock
Project: The purpose of this project is to establish a concept for the improvement of the I-86/I-15 IC complex. The Key #9000 project established a preliminary design study, IMR, and environmental clearance for this interchange. The intent of this project is to revisit Key 9000 geometry and revise and update to establish the final concept and scope of work for an FY22 project. It is estimated that \$50,000,000 will be needed for CN for this project paid out over FY22 and FY23. As many as 5 bridges will be addressed with this project
Status: The project is anticipated to have an intermediate design review in 2019 and be PS&E ready September 2020.

Project Name: FY 22 D5 Bridge Repair
Key: 20643 **Route:** Various **Mile Post:** Various **Eng C**
Counties: Various
Project: Bridge maintenance
Status: Preliminary bridge plans developed, roadway plans in development.

Project Name: **FY22 W. Bingham Co Pavement Preservation**
Key: 20597 **Route:** I-15/US-91/SH-39/US-26 **Mile Post:** Varies **Materials/Traffic**
Counties: Bingham County
Project: This project will rehabilitate and resurface pavement at various locations throughout Bingham County. This will be accomplished through pavement rehabilitation techniques and resurfacing.
Status: Design has not begun and is scheduled to start winter of 2019/2020 for a submittal in September of 2020.

FY 2023

Project Name: **Main St GS NBL & SBL, Inkom**
Key: 20547 **Route:** **I-15** **Mile Post:** 57.172-57.173 **Eng A**
Counties: Bannock
Project: This project will replace both the Northbound and Southbound structures on I-15 over Main Street in Inkom at milepost 57.172. They were originally built in 1962.
Status: This is being designed by HDR. HDR has completed the survey of the area and began borings in the area for the phase reports and sub/super-structure layouts. The local road underneath is being slightly lowered to allow more clearance under the I15 structure. Preliminary design review is scheduled for summer of 2020. Anticipated to be PS&E ready by Feb 2021. This is a FY2025.

Project Name: **US-26, Puzzle to MP 283**
Key: 20590 **Route:** US-26 **Mile Post:** 272.054 – 284.200 **Eng B**
Counties: Bingham and Butte
Project: CRABS
Status: A draft 1500 form has been completed. An Intermediate Design Review was held July 24, 2019. The design of special signs is being worked on. Anticipated to be PS&E ready by September 2019.

Project Name: **US-26, Moreland Rd to MP 303.5**
Key: 20481 **Route:** US-26 **Mile Post:** 301.538 – 303.500 **Eng B**
Counties: Bingham
Project: Widening
Status: Charter and project schedule are being developed. A kickoff meeting was held on March 5th. Discussions are in process to determine if Right-of-Way will be needed. Anticipated to be PS&E ready by Oct. 2021.

Project Name: **FY23 D5 Bridge Repair**
Key: 20636 **Route:** I-15 **Mile Post:** Various **Eng B**
Counties: Multiple
Project: Bridge preservation project on multiple structures.
Status: Charter and project schedule are being developed. Waiting on HQ Bridge for bridges. Anticipated to be PS&E ready by Oct. 2021.

Project Name: **Blackfoot Signal Upgrade**
Key: 20595 **Route:** I-15B **Mile Post:** Various **Materials/Traffic**
Counties:

Project: This project will include the installation of a new signal cabinet, mast arms, and will upgrade the signals to modern equipment on the ITD system throughout Blackfoot.
Status: Working on a trial run of eliminating a signal in Blackfoot. Planning for fiber is ongoing with utility companies. Plan sheets have been started. Anticipated to be PS&E ready by March 2021.

Project Name: **FY23 E. Bingham Co Pavement Preservation**
Key: 20415 **Route:** I-15/US-91/SH-39/US-26 **Mile Post:** Varies **Materials/Traffic**
Counties: Bingham

Project: This project will place a seal coat on various roads in eastern Bingham Co. The seal coat extends pavement life by stopping water from penetrating the roadway. It also enhances safety by increasing skid resistance.
Status: Design has not begun and is scheduled to start winter of 2020/2021 for a submittal in September of 2021.

Project Name: **D5 Wildlife Fence**
Key: 20437 **Route:** US-30 **Mile Post:** 371.77 – 375.958 **Materials/Traffic**
Counties: Bannock

Project: This project will install wildlife fence and jump outs along US-30.
Status: The existing fence has been measured. A meeting with Fish and Game is planned to figure where to install jump outs. Design is scheduled to be complete September 2019.

FY 2024

Project Name: **US-91, FY24 Blackfoot Canal**
Key: 20447 **Route:** **US-91** **Mile Post:** 113.255 **Eng A**
Counties: Bingham

Project: This project will replace the Blackfoot Canal Bridge on US-91 at milepost 113.255. It was originally built in 1951
Status: Charter and project schedule are being developed. Anticipated to be PS&E ready by Oct. 2022 as it is a FY2025 project.

Project Name: **US-30, Rocky Point Wildlife Xings**
Key: 22127 **Route:** US-30 **Mile Post:** **Eng A**
Counties:

Project: This project will install new/original wildlife crossing on US-30 North of Georgetown. This area is a primary wildlife crossing area and safety/road user costs justify the installment of 1-2 crossings.
Status: Charter and project schedule are being developed. It is unclear whether under or over crossing will be utilized at this point. Anticipated to be PS&E ready by Oct. 2022 as it is a FY2025 project.

Project Name: **SH-39, FY24 Wasteway Canal**
Key: 20609 **Route:** SH-39 **Mile Post:** 6.905 **Eng B**
Counties: Power

Project: This project will replace the Wasteway Canal Bridge on SH-39 at milepost 6.905. It was originally built in 1930.

Status: Project is anticipated to be PS&E ready Sept 2023. Preliminary design not to start until 2021

Project Name: **FY24 D5 Bridge Repair**
Key: 20705 **Route:** State **Mile Post:** Various **Eng C**
Counties:

Project: This project will provide bridge deck preservation and preventative maintenance to the bridges, bridge approaches and guardrail in various locations throughout District 5.

Status: Charter and project schedule are being developed. Anticipated to be PS&E ready by Oct. 2022.

Project Name: **I-15, Rose Rd IC to N Lava Rocks**
Key: 20688 **Route:** I-15 **Mile Post:** 97.992 – 104.202 **Eng C**
Counties: Bingham

Project: This project is a pavement rehabilitation project designed to fix cracking and rutting and prolong the pavement lifecycle of I-15.

Status: Design scheduled to begin in FY22.

Project Name: **US-91, FY24 Park lawn to Siphon Rd**
Key: 21860 **Route:** US-91 **Mile Post:** **Materials/Traffic**
Counties: Bannock

Project: This project is a widening project that will provide additional capacity along Yellowstone Avenue between Park Lawn and Siphon. It will also allow for the addition of a traffic signal at the intersection of Yellowstone Avenue and Siphon Road

Status: Planning meetings have been held with the City of Chubbuck along with a value planning study. An option has been chosen, thru U-turns. We are currently in the process of hiring a surveyor to help with modeling the corridor and right of way purchases.

FY 2025

Project Name: **McCammon IC to Old US-91**
Key: 21832 **Route:** I-15B **Mile Post:** 359.5 – 359.7 **Eng A**
Counties: Bannock

Project: This project is a restoration and resurfacing designed to extend the pavement lifecycle on I-15 Business Loop in McCammon between mileposts 0 and .494.

Status: Charter and project schedule are being developed. Anticipated to be PS&E ready by Oct. 2022 as it is a FY2025 project.

Project Name: **FY25 D5 Bridge Repair**
Key: 21874 **Route:** **Mile Post:** **Eng A**
Counties:

Project: Bridge Repairs throughout the District.

Status: Charter and project schedule are being developed. Anticipated to be PS&E ready by Oct. 2022 as it is a FY2025 project.

Project Name: **US-30, FY25 Nounan Rd to Bennington**
Key: 21895 **Route:** US-30 **Mile Post:** 424.5-430 **Eng A**

Counties: Bear Lake
Project: This project is a Cement Recycled Asphalt Base Stabilization. The idea is to grind the existing highway down to the base and add cement thereby reinforcing the stability of the highway and enhancing the lifecycle of US-30 between mileposts 424.5 and 430
Status: Charter and project schedule are being developed. Anticipated to be PS&E ready by Oct. 2022 as it is a FY2025 project.





Project Name: **FY25 Oneida Co Pavement Preservation**
Key: 21815 **Route:** **Mile Post:** **Eng A**
Counties: Oneida
Project: Prolong the life and increase skid resistance of state highway pavements within Oneida Co. by applying a seal coat over existing road surfaces.
Status: Charter and project schedule are being developed. Anticipated to be PS&E ready by Oct. 2022 as it is a FY2025 project.





Project Name: **US-91, FY25 Yellowstone Ave; Breneman to Knudsen**
Key: 21911 **Route:** Bannock **Mile Post:** **Eng A**
Counties:
Project: This is a safety project with a scope of constructing a concrete median, thereby disallowing left hand turns across multiple lanes of traffic.
Status: Charter and project schedule are being developed. Anticipated to be PS&E ready by Oct. 2022 as it is a FY2025 project.

Project Name: **I-15, Inkom IC NBL & SBL**
Key: 21872 **Route:** I-15 **Mile Post:** 6.905 **Eng C**
Counties: Bannock
Project: This project will be an Interchange Replacement on Interstate 15 in Inkom.
Status: Preliminary concepts have been developed. ITD staff has attended Inkom city council meetings to make them aware of the upcoming project and to coordinate the project with the city of Inkom's transportation plan being developed by Keller Associates.

TH:bp/mh
rf *electronic*

ATTACHMENT D

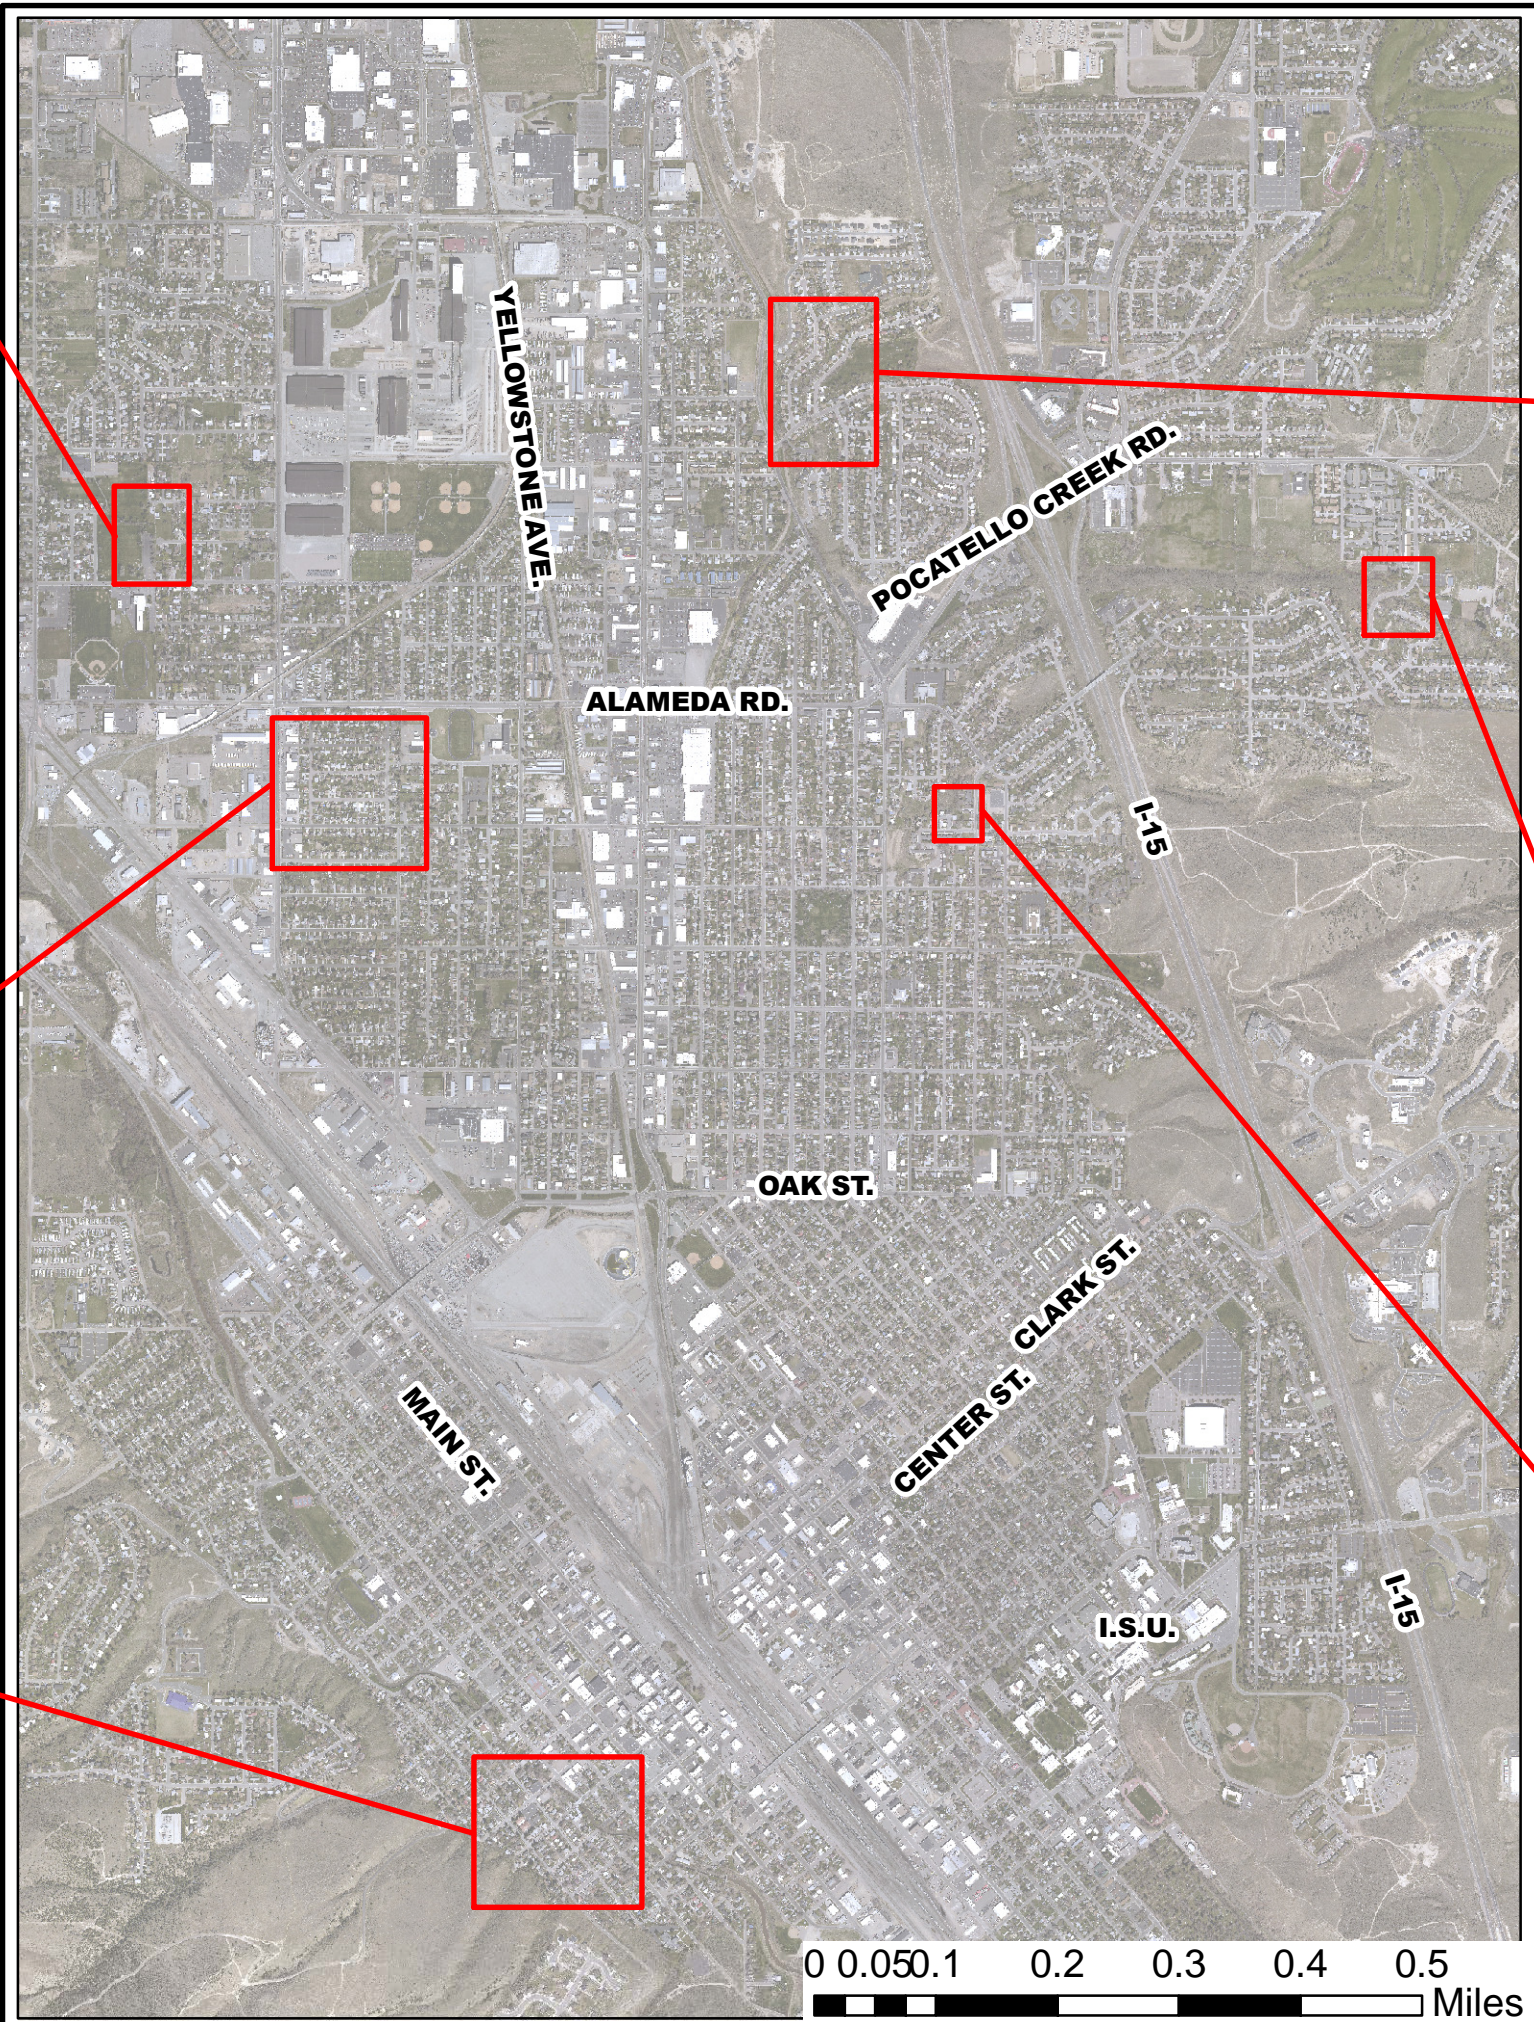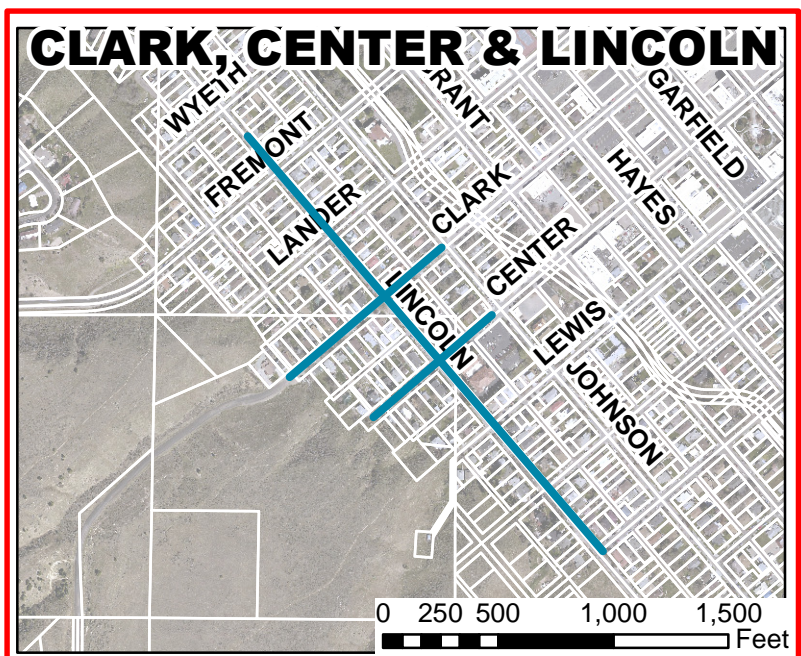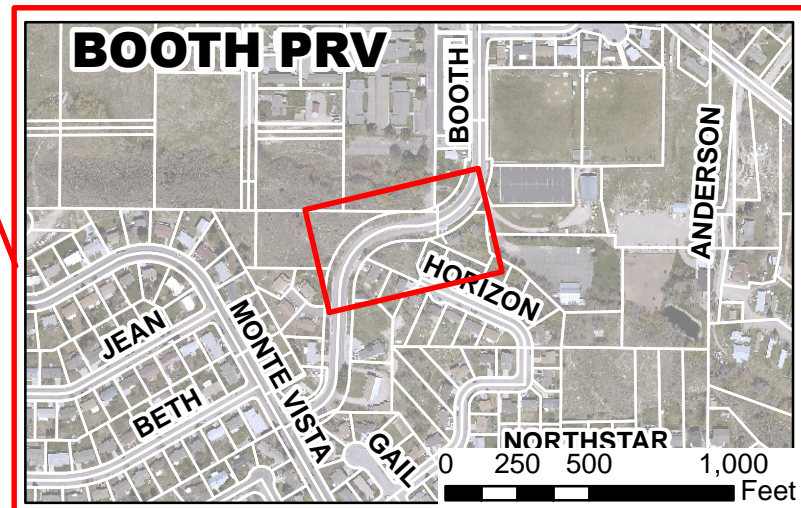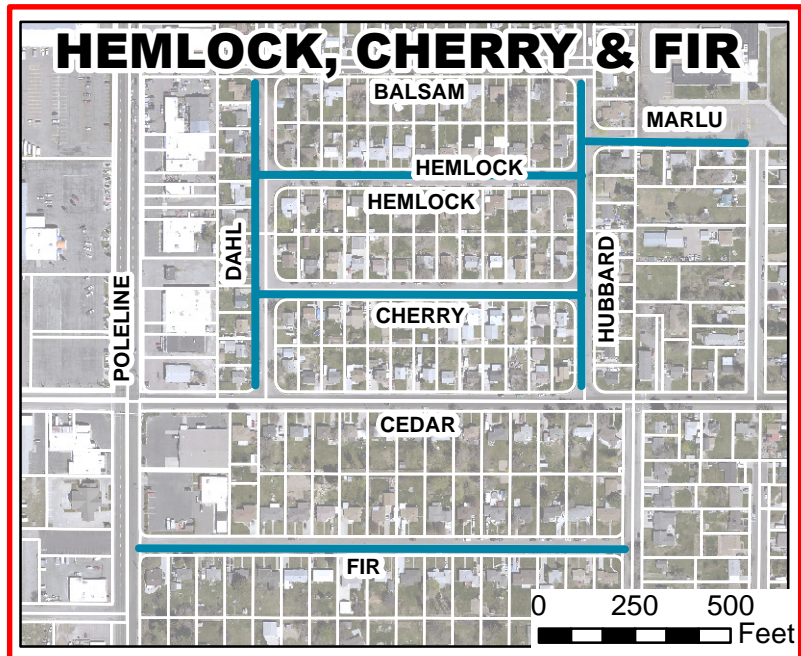

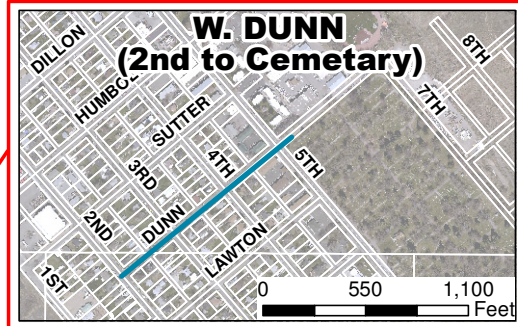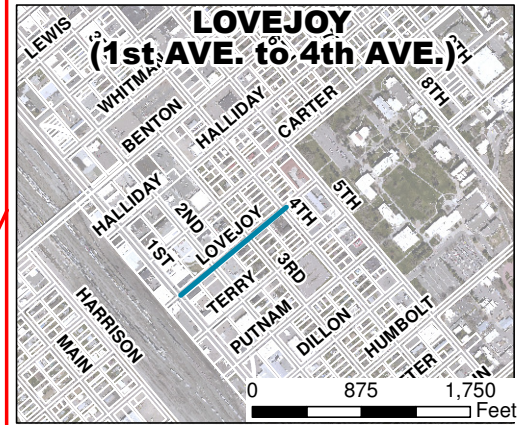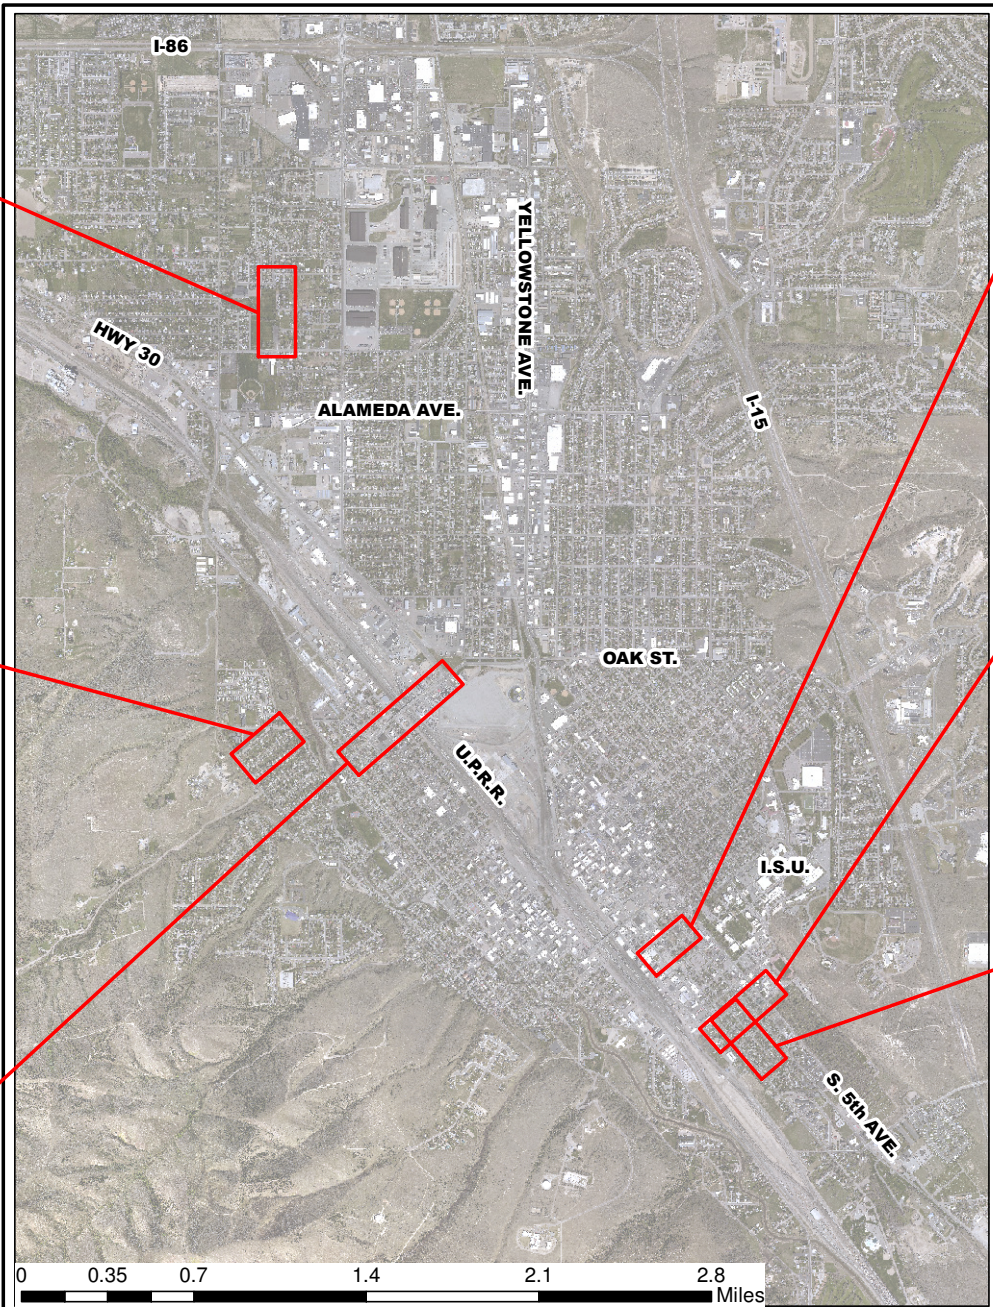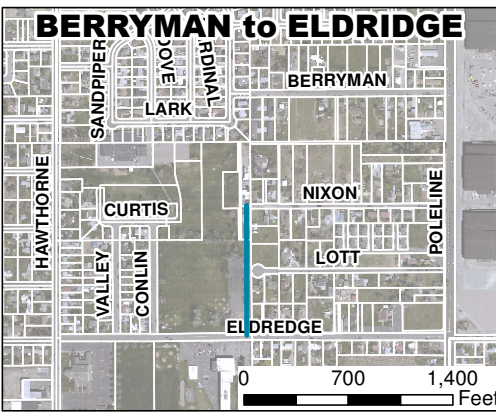

2020 PROJECT LOCATION MAP
POCATELLO WATER DEPT.
PREPARED BY: B. HOCH
